




	Name	Dauer	Start	Ende	Vorgä...	30 Sep 24							7 Okt 24							14 Okt 24							21 Okt 24												
						S	S	M	D	M	D	F	S	S	M	D	M	D	F	S	S	M	D	M	D	F	S	S	M	D	M	D	F	S	S				
1	Baustelle Einrichten	3 tage	01.10.24 08:00	04.10.24 15:00																																			
2	Abbrucharbeiten	5 tage	04.10.24 15:00	14.10.24 15:00	1																																		
3	Aushub	3 tage	14.10.24 15:00	18.10.24 10:00	2																																		
4	Pufferzeit	5 tage	18.10.24 10:00	28.10.24 10:00	3																																		
5	Einbauen	2 tage	28.10.24 10:00	30.10.24 15:00	4																																		
6	Fundamente, Bodenplatte	15 tage	30.10.24 15:00	25.11.24 15:00	5																																		
7	Mauerwerk	10 tage	25.11.24 15:00	11.12.24 15:00	6																																		
8	Decke	5 tage	11.12.24 15:00	19.12.24 15:00	7																																		
9	Pufferzeit	31 tage	19.12.24 15:00	10.02.25 17:00	8																																		
10	Mauerwerk D, Attika	10 tage	10.02.25 17:00	26.02.25 17:00	9																																		
11	Zimmerer/Dachdecker/Spengler Steildach	15 tage	26.02.25 17:00	24.03.25 17:00	10																																		
12	Schwarzdecker	10 tage	24.03.25 17:00	09.04.25 17:00	11																																		
13	Fenster	15 tage	09.04.25 17:00	05.05.25 17:00	12																																		
14	Außenputz	20 tage	05.05.25 17:00	06.06.25 17:00	13																																		
15	Pufferzeit	10 tage	06.06.25 17:00	24.06.25 17:00	14																																		
16	Spengler	15 tage	24.06.25 17:00	18.07.25 17:00	15																																		
17	Außenanlagen	25 tage	18.07.25 17:00	29.08.25 17:00	16;35																																		
19	Innenwände	10 tage	10.02.25 17:00	26.02.25 17:00	9																																		
20	Trockenbau	5 tage	26.02.25 17:00	06.03.25 17:00	19																																		
21	Heizung-/Sanitärinstallation	10 tage	06.03.25 17:00	24.03.25 17:00	20																																		
22	Elektroinstallation	10 tage	24.03.25 17:00	09.04.25 17:00	21																																		
23	Innenputz	10 tage	09.04.25 17:00	25.04.25 17:00	22																																		
24	Pufferzeit	5 tage	25.04.25 17:00	05.05.25 17:00	23																																		
25	Estrich	7 tage	05.05.25 17:00	16.05.25 10:00	24																																		
26	Pufferzeit	10 tage	16.05.25 10:00	03.06.25 10:00	25																																		
27	Trockenbau	10 tage	03.06.25 10:00	19.06.25 10:00	26																																		
28	Heizung-/Sanitärinstallation	10 tage	19.06.25 10:00	07.07.25 10:00	27																																		
29	Elektroinstallation	10 tage	07.07.25 10:00	23.07.25 10:00	28																																		
30	Pufferzeit	5 tage	23.07.25 10:00	31.07.25 10:00	29																																		
31	Böden	10 tage	31.07.25 10:00	18.08.25 10:00	30																																		
32	Ausstattung	8 tage	18.08.25 10:00	29.08.25 17:00	31																																		
33	Komplettierung	8 tage	18.08.25 10:00	29.08.25 17:00	31																																		
35	Entwässerungsanlage	20 tage	28.10.24 10:00	29.11.24 10:00	4																																		




28 Okt 24				4 Nov 24				11 Nov 24				18 Nov 24				25 Nov 24				2 Dez 24				9 Dez 24				16 Dez 24				23 Dez 24				30 Dez 24																
S	M	D	M	D	F	S	S	M	D	M	D	F	S	S	M	D	M	D	F	S	S	M	D	M	D	F	S	S	M	D	M	D	F	S	S	M	D	M	D	F	S	S	M	D	M	D	F	S	S	M	D	M

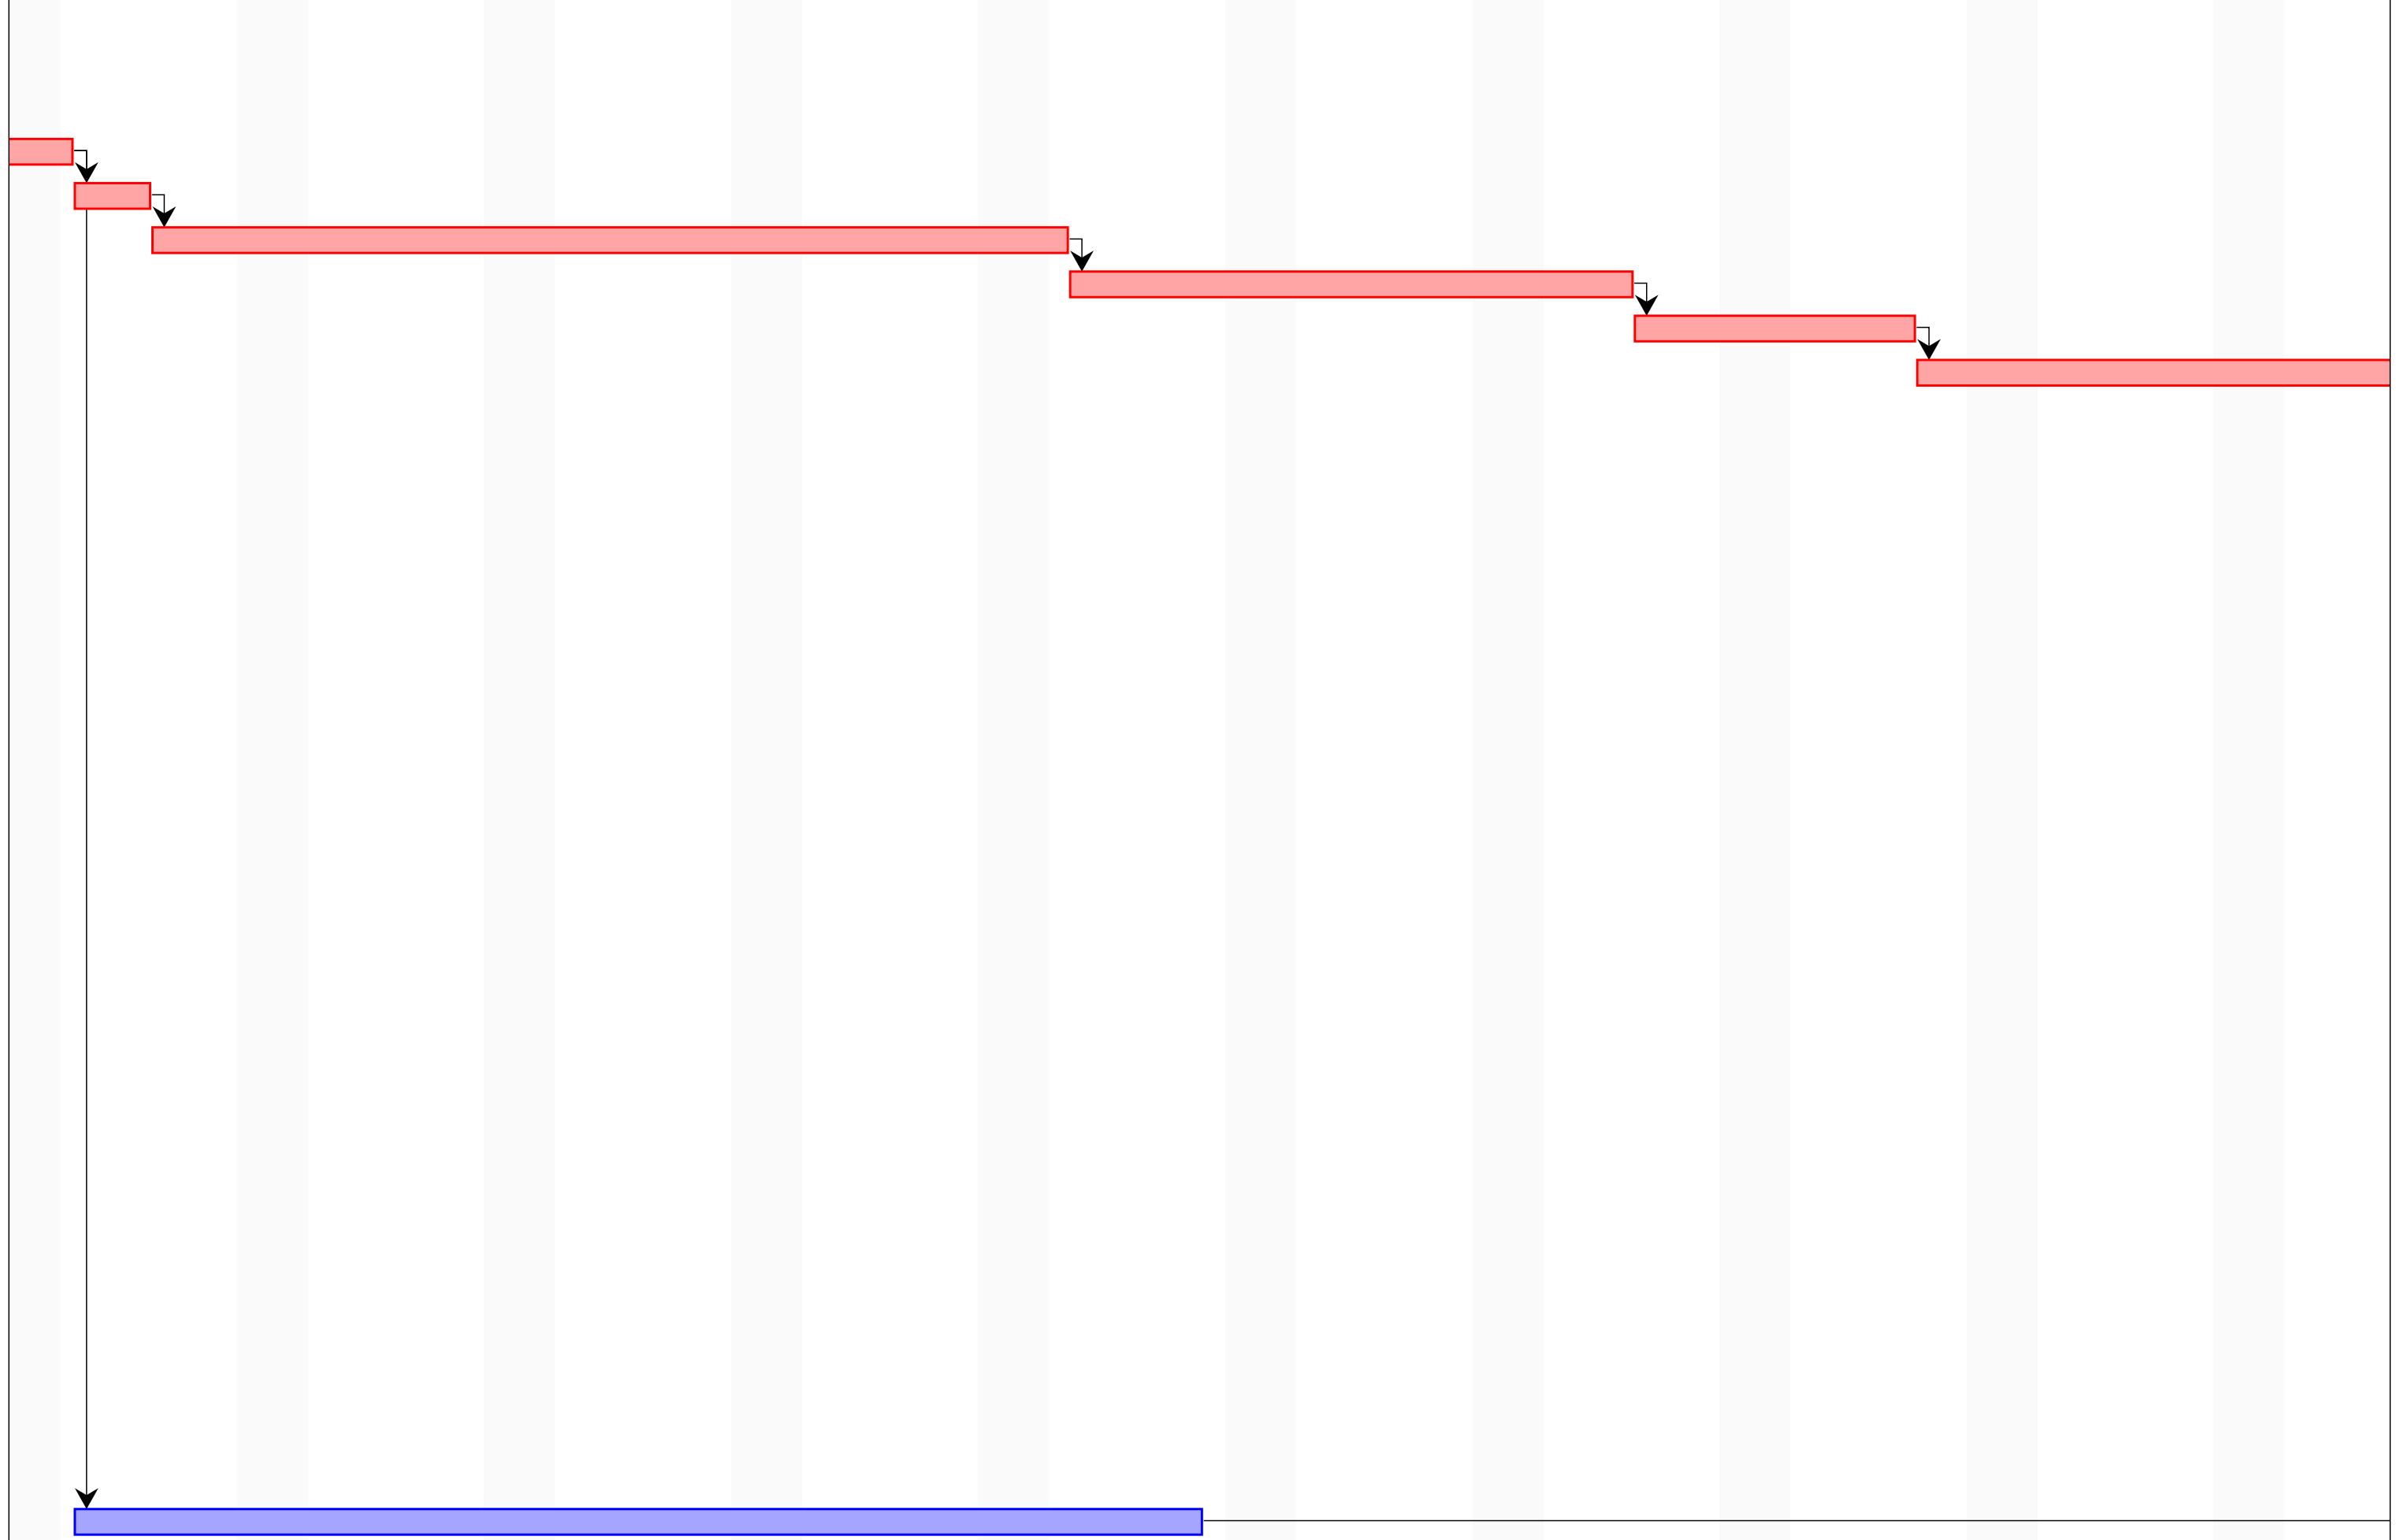


4	6 Jän 25					13 Jän 25					20 Jän 25					27 Jän 25					3 Feb 25					10 Feb 25					17 Feb 25					24 Feb 25					3 Mär 25					1													
D	F	S	S	M	D	M	D	F	S	S	M	D	M	D	F	S	S	M	D	M	D	F	S	S	M	D	M	D	F	S	S	M	D	M	D	F	S	S	M	D	M	D	F	S	S	M	D	M	D	F	S	S	M	D	M	D	F	S	S

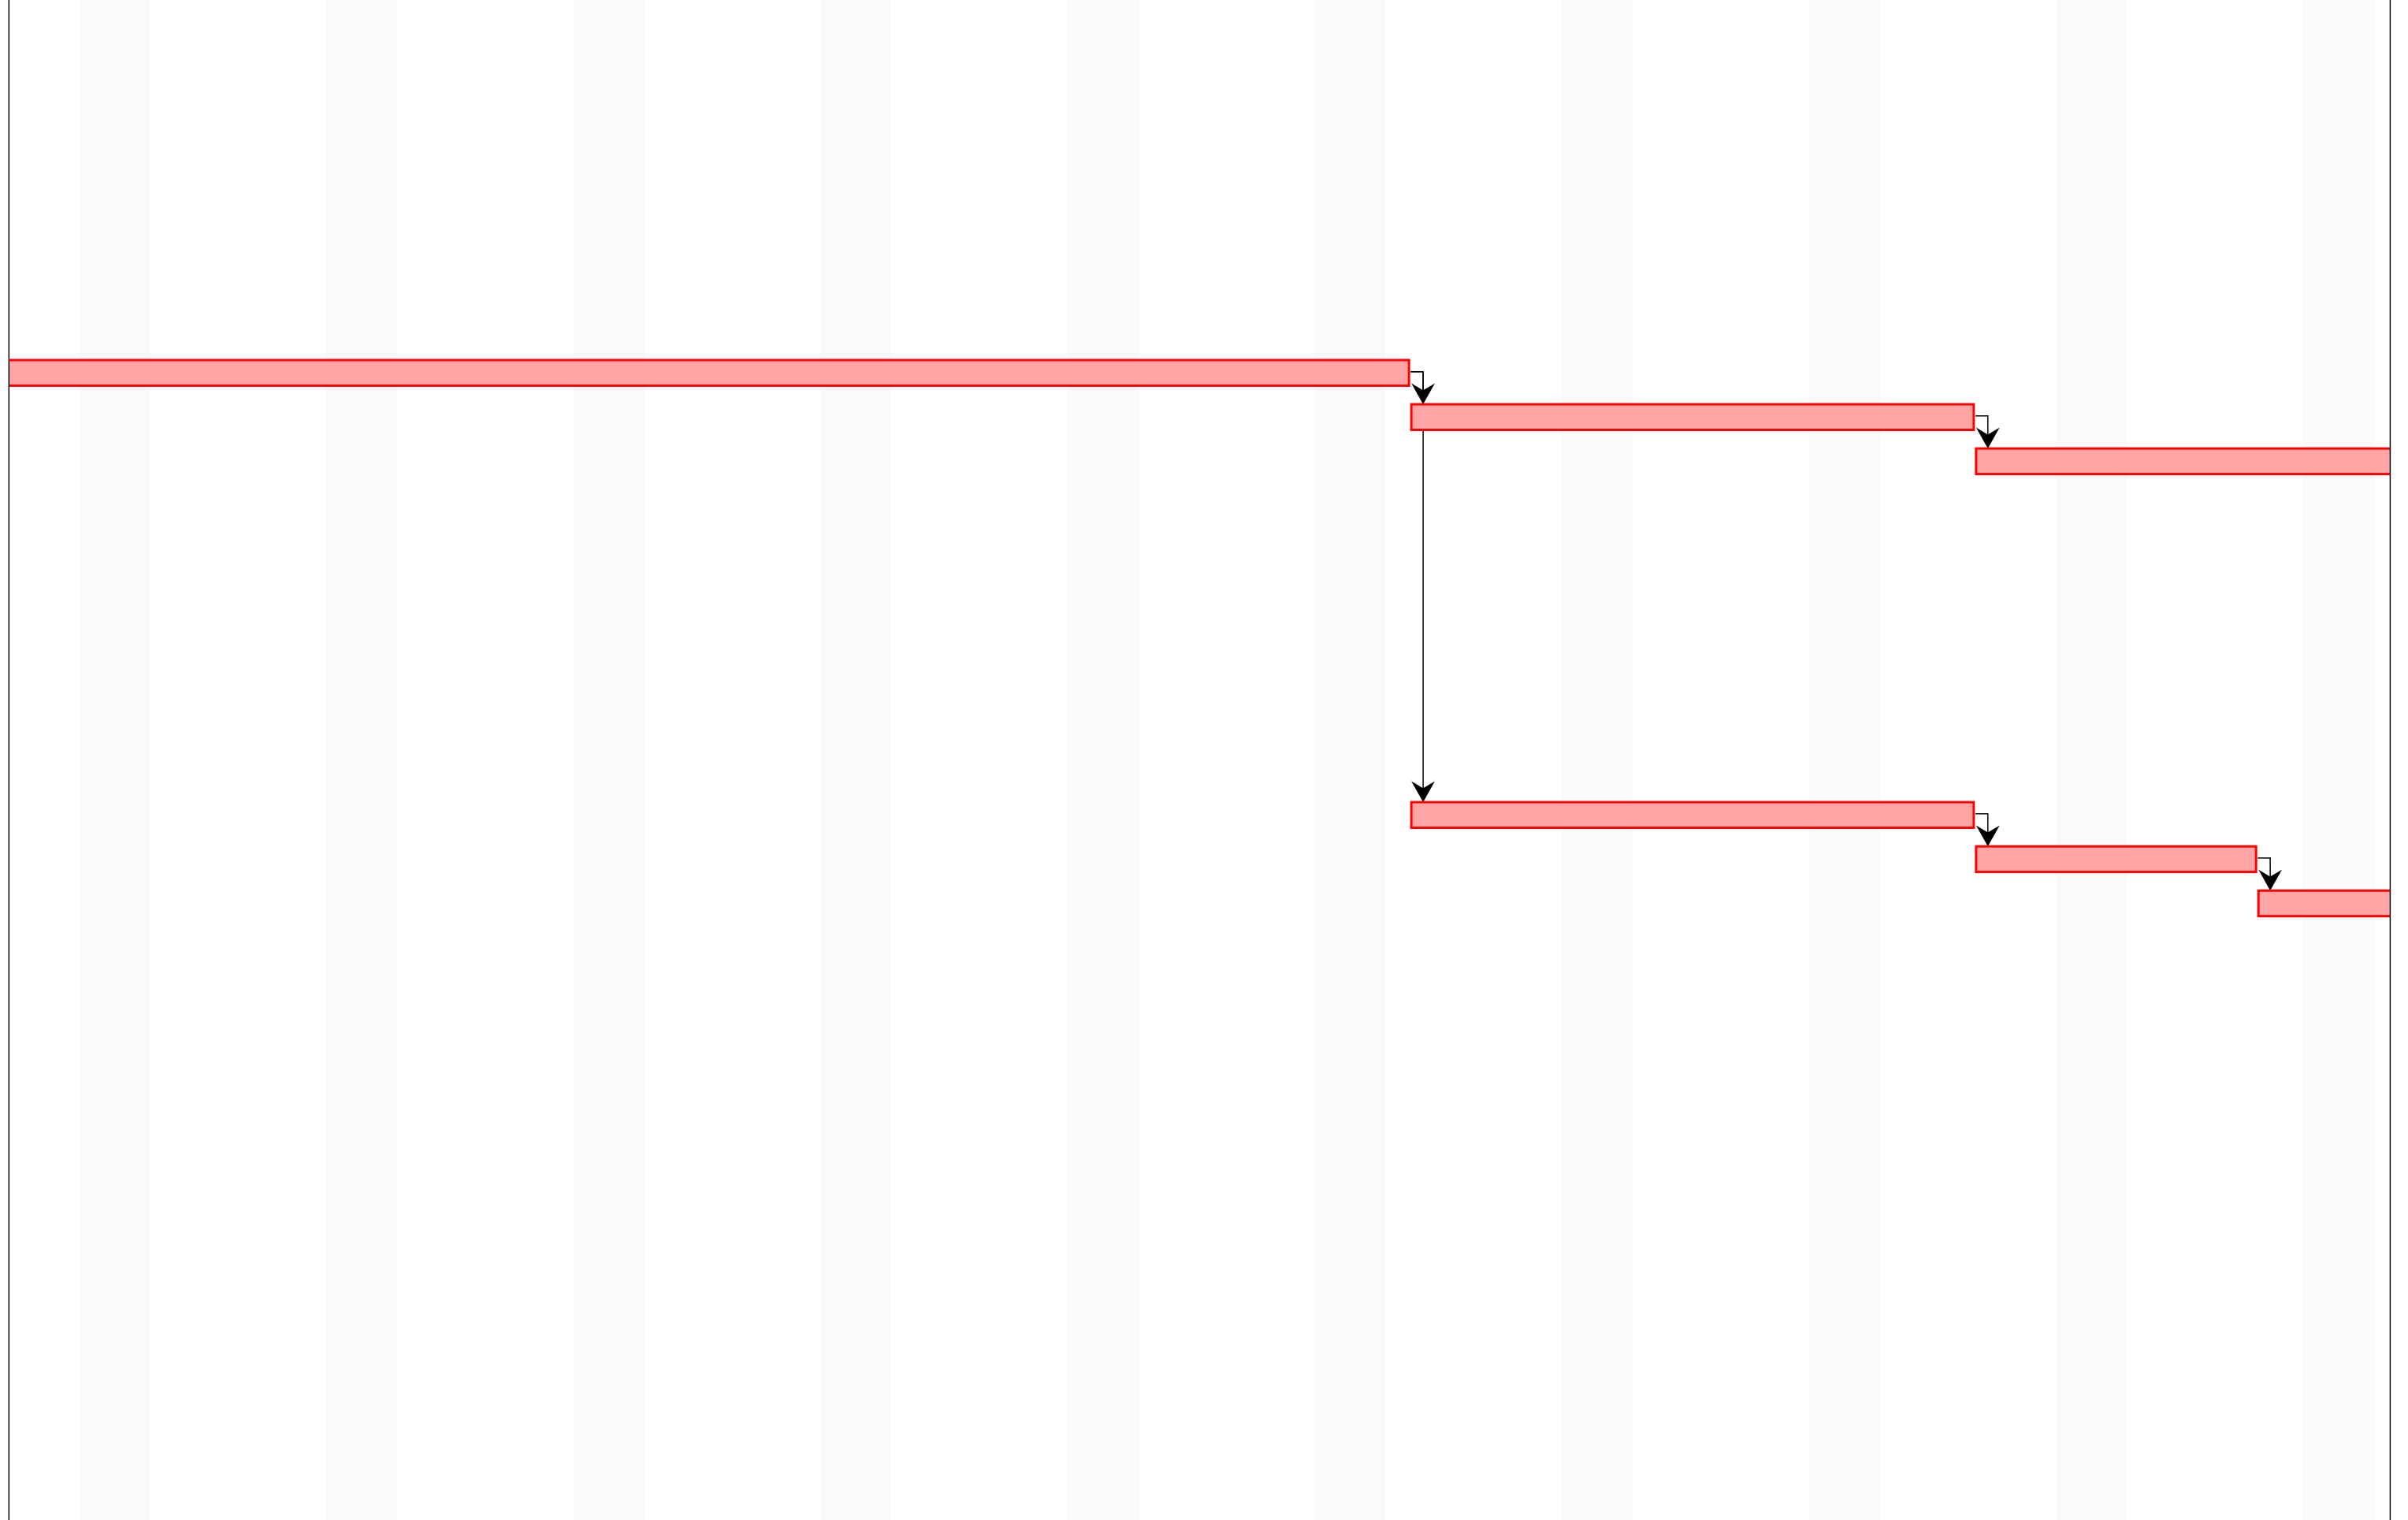

0 Mär 25					17 Mär 25					24 Mär 25					31 Mär 25					7 Apr 25					14 Apr 25					21 Apr 25					28 Apr 25					5 Mai 25					12 Mai 25																	
M	D	M	D	F	S	S	M	D	M	D	F	S	S	M	D	M	D	F	S	S	M	D	M	D	F	S	S	M	D	M	D	F	S	S	M	D	M	D	F	S	S	M	D	M	D	F	S	S	M	D	M	D	F	S	S	M	D	M	D	F	S	S

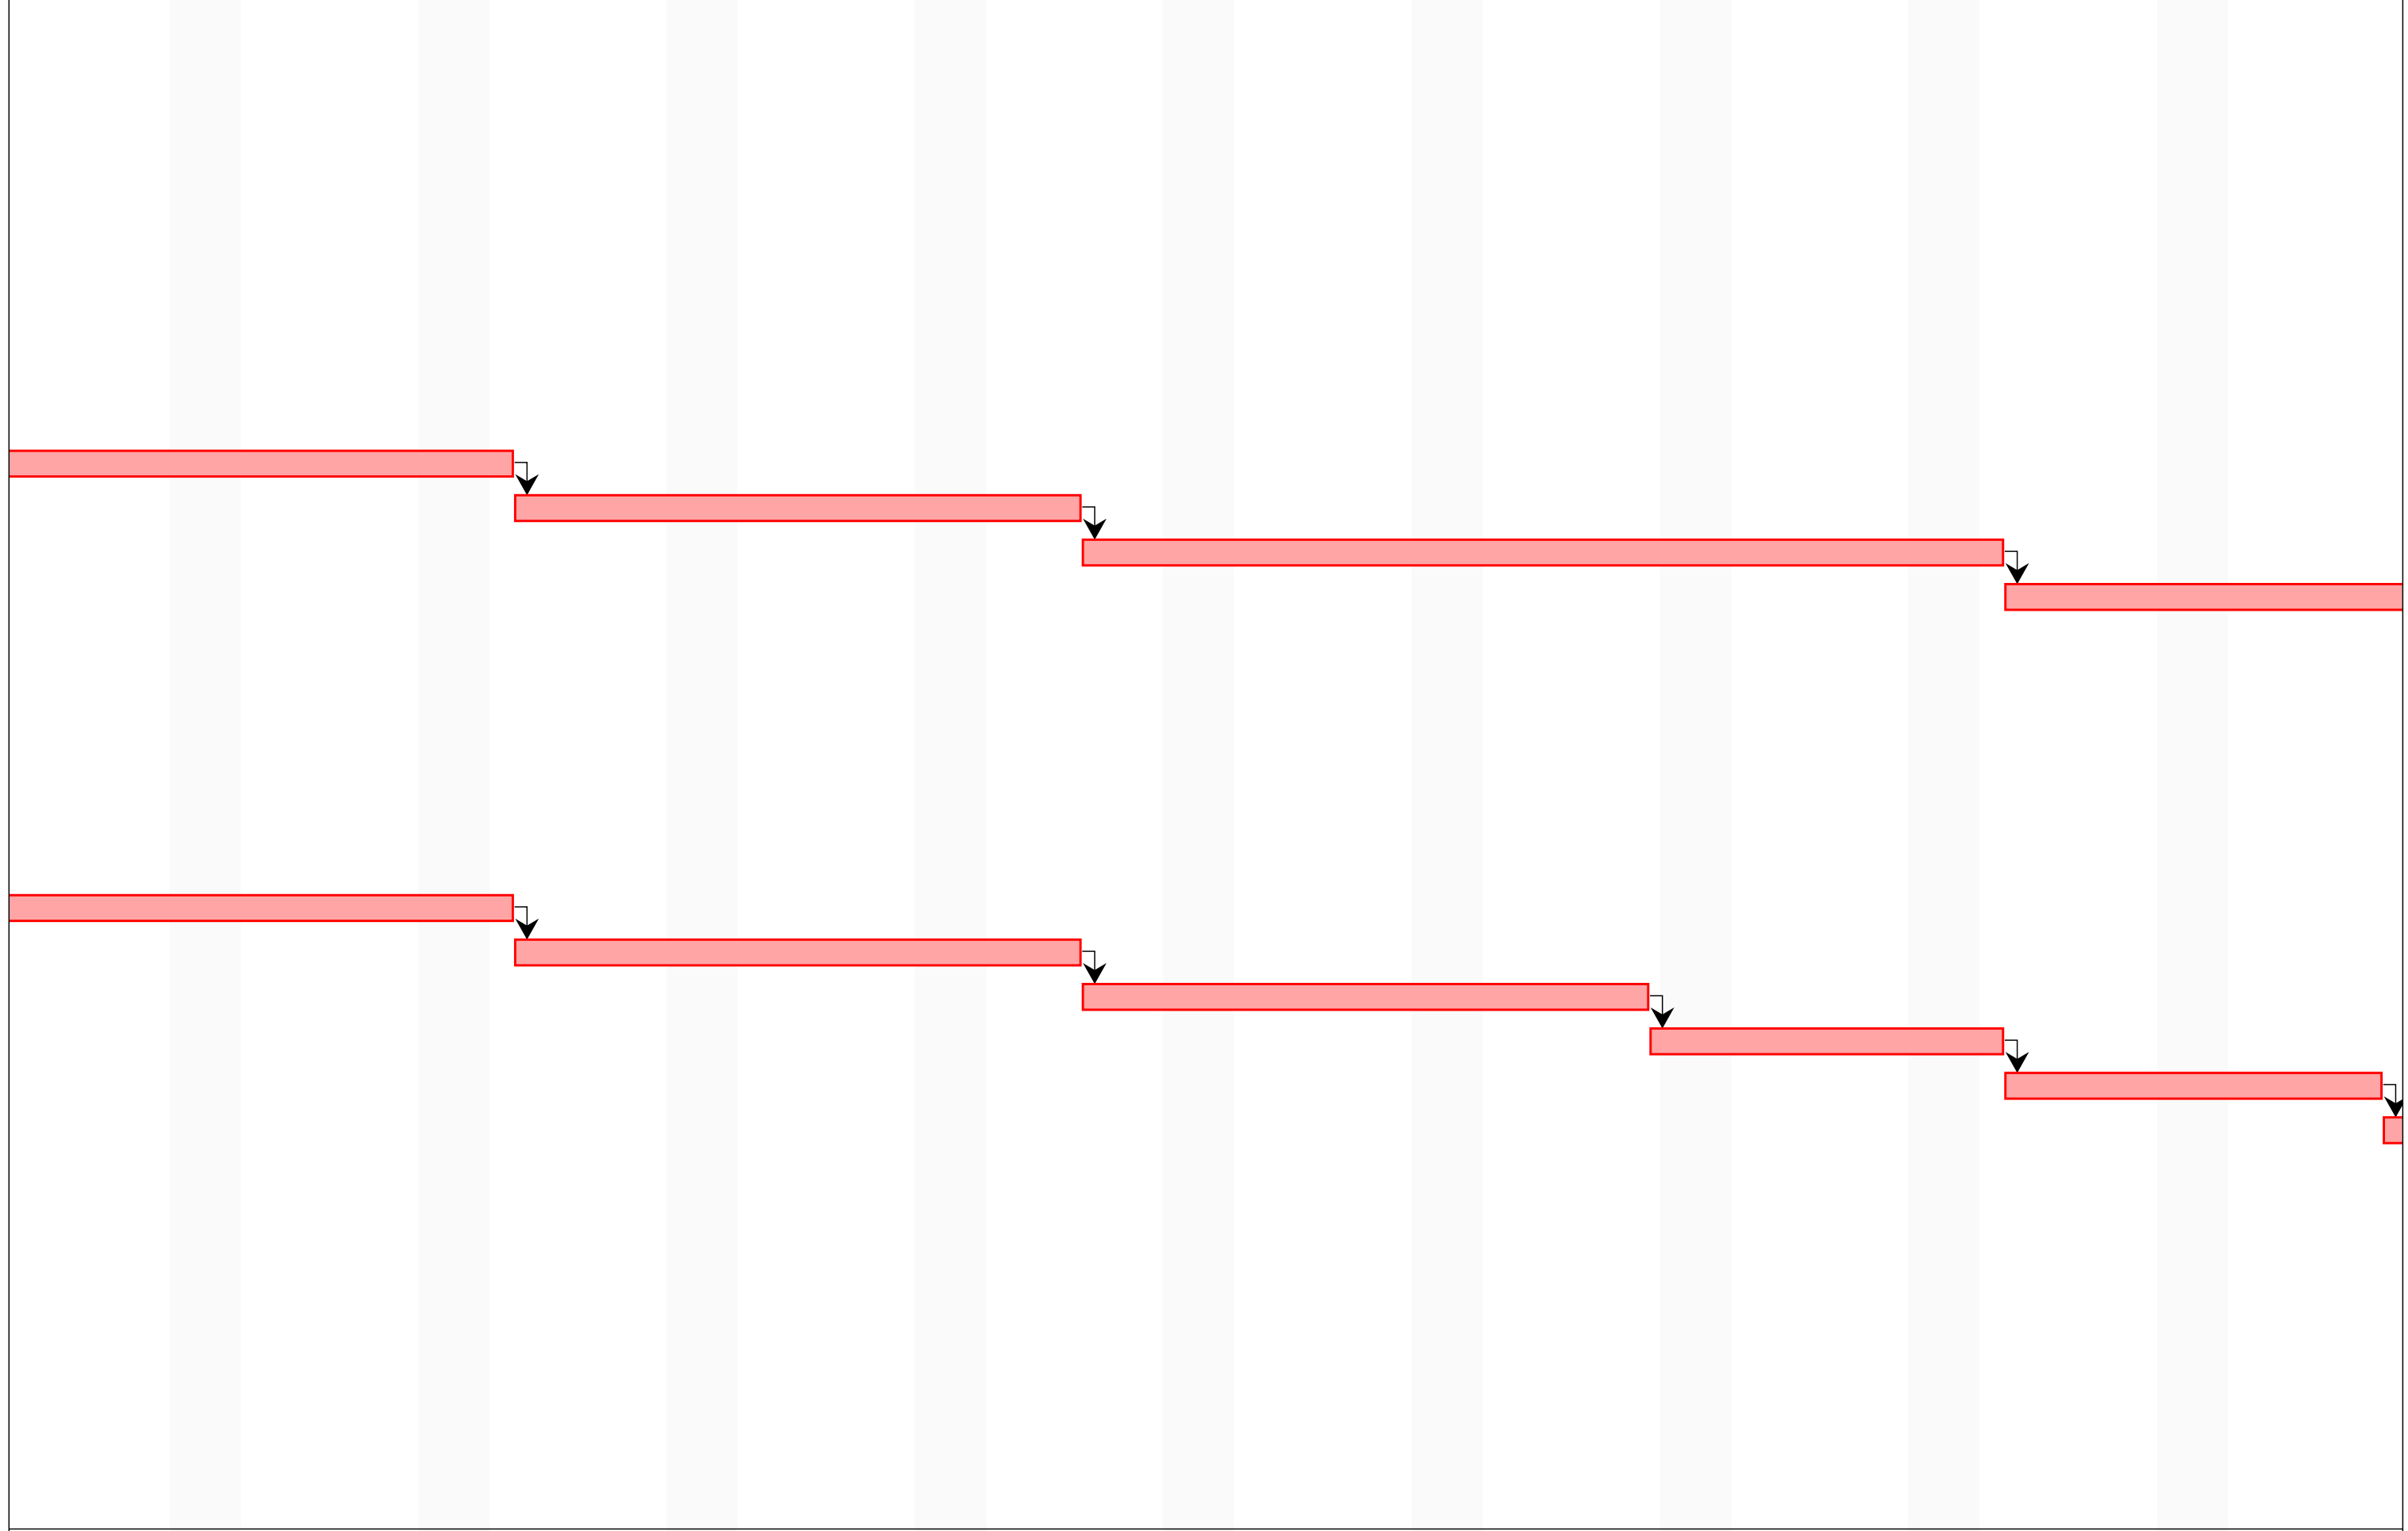

	19 Mai 25				26 Mai 25				2 Jun 25				9 Jun 25				16 Jun 25				23 Jun 25				30 Jun 25				7 Jul 25				14 Jul 25				21 Jul 25																				
S	S	M	D	M	D	F	S	S	M	D	M	D	F	S	S	M	D	M	D	F	S	S	M	D	M	D	F	S	S	M	D	M	D	F	S	S	M	D	M	D	F	S	S	M	D	M	D	F	S	S	M	D	M	D	F	S	S

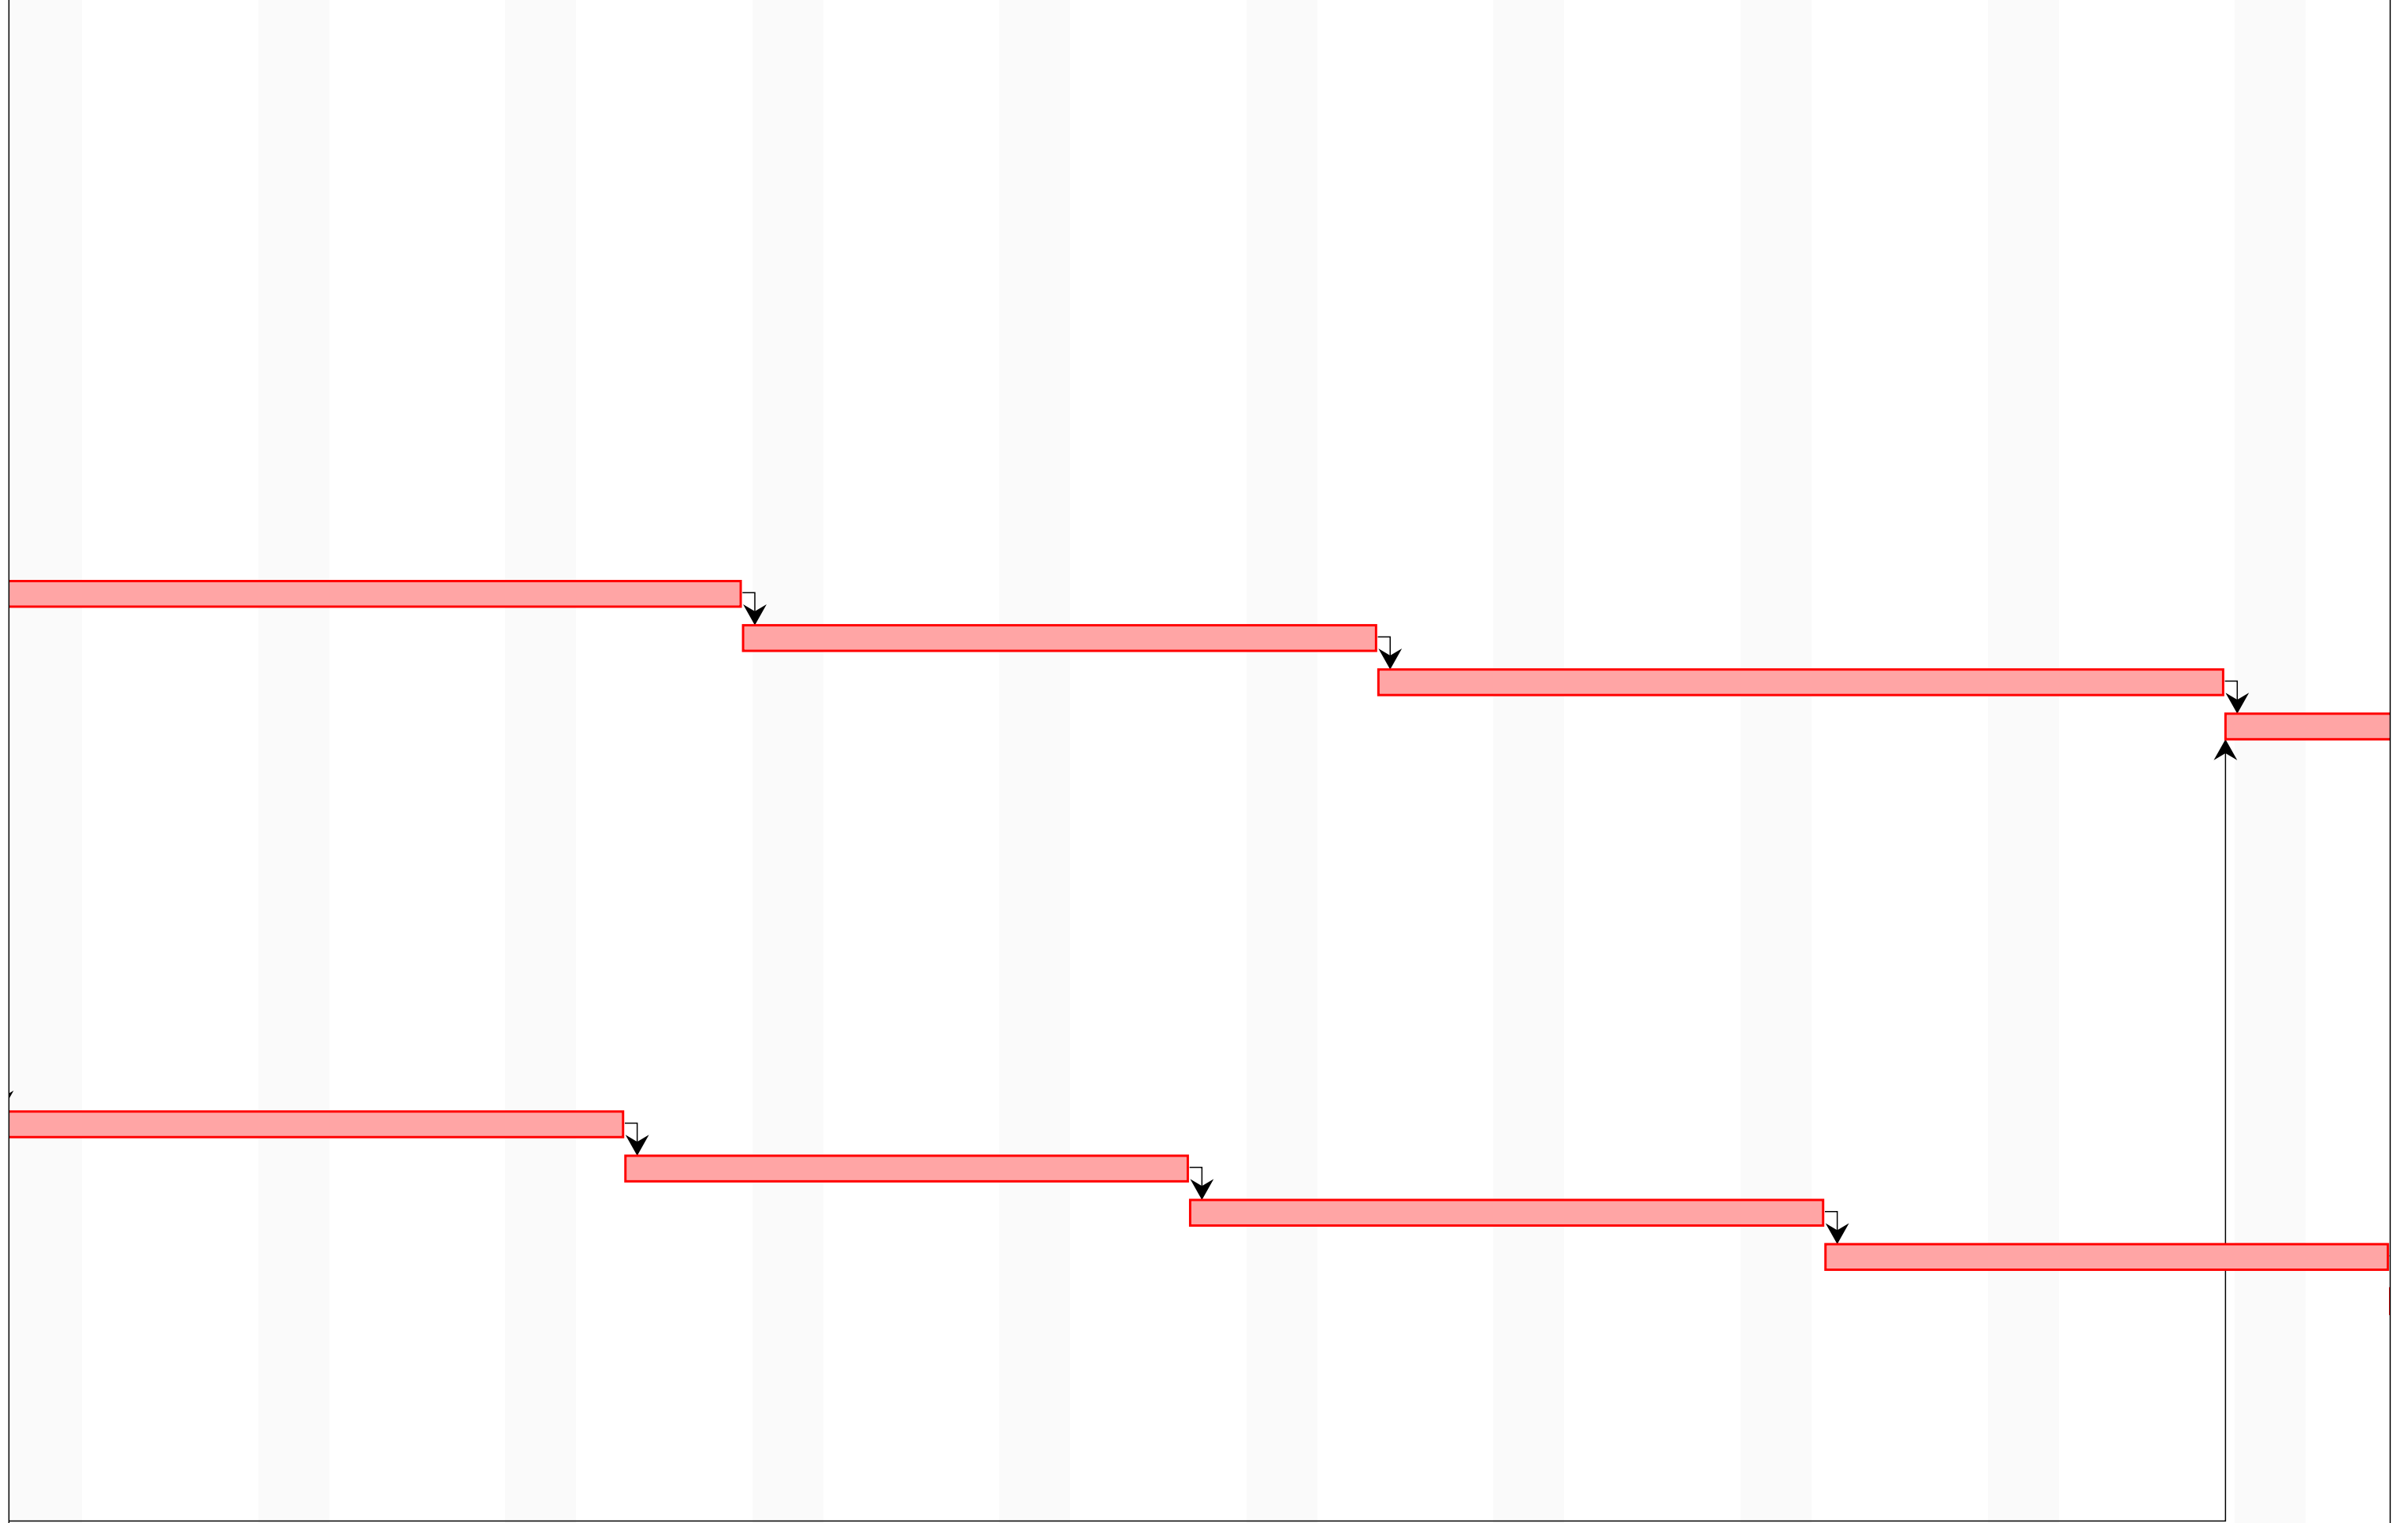

25	28 Jul 25	4 Aug 25	11 Aug 25	18 Aug 25	25 Aug 25	1 Sep 25	8 Sep 25	15 Sep 25	22 Sep 25
M D F S S	M D M D F S S	M D M D F S S	M D M D F S S	M D M D F S S	M D M D F S S	M D M D F S S	M D M D F S S	M D M D F S S	M D M D F S S

